Cooper Lake Project Relicensing
Settlement Negotiations and
Remaining Process Steps

ID	Task Name	Finish
1	**Major relicensing process milestones**	**Fri 4/15/05**
2	Draft license application issued	Mon 5/31/04
3	Workshop on DLA	Wed 7/14/04
4	Comments due on DLA	Thu 9/30/04
5	Review of comments received on DLA	Fri 10/29/04
6	Window for holding dispute resolution meeting(s)	Tue 11/30/04
7	Final license application (FLA) preparation	Thu 3/31/05
8	Suspend negotiations to finalize FLA	Fri 4/15/05
9	Preliminary CZMA consistency determination	Tue 3/22/05
10	FLA filed with FERC	Fri 4/15/05
11		
12	**Availability of outstanding technical information**	**Mon 11/15/04**
13	Water temperature/flow data collection	Mon 11/15/04
14	Cooper Creek fall spawning surveys	Mon 11/15/04
15	Cooper Creek habitat modeling	Mon 11/15/04
16	Cooper Creek engineering concepts analysis	Mon 11/15/04
17	Mapping of sensitive plants	Mon 11/15/04
18	Road and Access Route Condition Survey	Mon 11/15/04
19	Archaeological surveys of t-line access routes	Mon 11/15/04
20		
21	**Settlement negotiations related activity**	**Wed 8/31/05**
22	Notice of negotiations planning meeting	Fri 8/20/04
23	Negotiations planning meeting	Thu 9/2/04
24	Approval of negotiations protocol	Thu 9/30/04
25	Pre-application filing negotiations	Tue 2/1/05
26	Finalize Agreement in Principle	Mon 2/28/05
27	File Agreement in Principle	Fri 4/15/05
28	Develop final Settlement Agreement	Wed 8/31/05
29	File final Settlement Agreement with FERC	Wed 8/31/05
30		
31	**Anticipated FERC processing steps**	**Mon 4/30/07**
32	Complete initial review of application/issue AIRs if needed	Thu 6/30/05
33	Notice of complete appl.; ready for env. Anal.; request terms/conditions	Fri 7/29/05
34	FERC prepares and issues NEPA document	Wed 5/3/06
35	Comment period on NEPA document	Fri 6/30/06
36	Conduct Section 10(j) process	Mon 7/31/06
37	Curent license expires	Mon 4/30/07

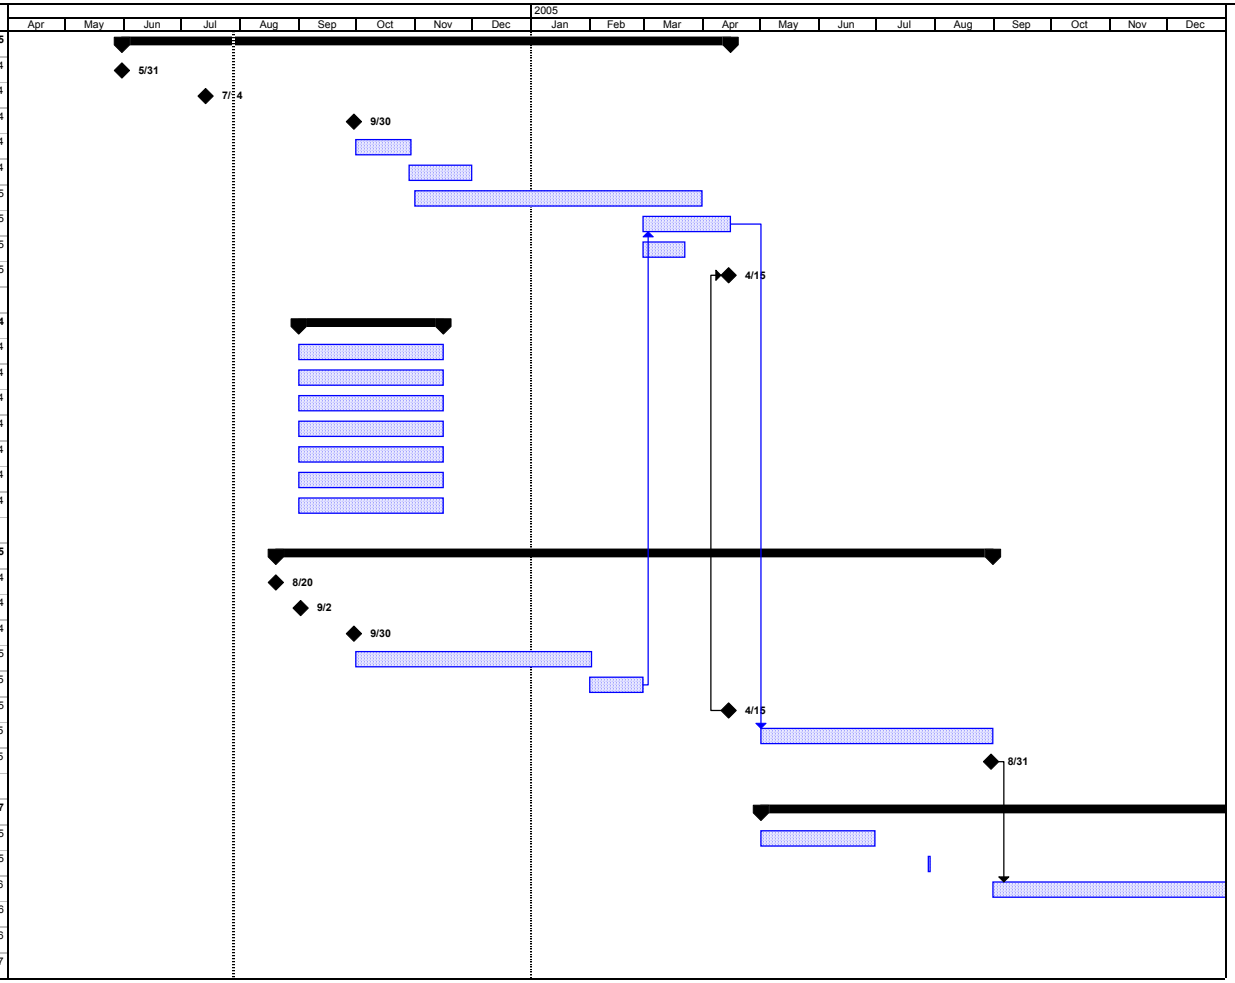

Project: CL PME Analysis
Date: Wed 7/28/04

Task | Progress | Summary | Rolled Up Split | Rolled Up Progress | Project Summary
Split | Milestone | Rolled Up Task | Rolled Up Milestone | External Tasks
